



P.O. Box 32071  
Kampala - Uganda

**Tusaidiane Uganda Limited**  
Management Advisory & Implementation Services  
[www.tusaidiane.com](http://www.tusaidiane.com) / Mobile: +256752766402  
Certificate of Incorporation No. 97141  
e-Tin 100011344 / URA File no. 99865

Email: [tul.sharifa@gmail.com](mailto:tul.sharifa@gmail.com)

25<sup>th</sup> of May 2021

## STATUS REPORT FOR THE CONSTRUCTION OF DORMITORIES FOR P7 GIRLS AND BOYS / KACHICA ACTION PLAN 2020



On Thursday, the 20<sup>th</sup> of May, Tusaidiane visited Kamuli Childcare Nursery and Primary School (KAHICA) to inspect construction issues. One of them was the status of construction of dormitories.

The picture above shows the construction site with left the Boys Dormitory under construction and right the Girls Dormitory. Above the Girls Dorm you see the Kitchen with tanks and the Main Hall.

The three people in the middle are Josephine of school management, constructor Ibrahim Haumba and Tusaidiane Consultant Rachel.

The inspection team was composed of Consultant Rachel Tushabe (also Administrator of the Tusaidiane Trust) and Kees Ebskamp, Chairman Tusaidiane Uganda and the Tusaidiane Trust.

The construction of the dormitories was started early April in the Easter weekend in view of the expected rainy season with the procurement of Kampala materials and the procurement of local materials.

That showed to be a wise decision because rain during April and early May has thwarted construction.

A week earlier the inspection team could not reach Kamuli and had to return to Kampala.

Roads are severely demolished. The trip forth and back takes 10 to 11 hours driving.



Girls  
right




and

←  
Left the  
Boys.





The ground plan for both dormitories is the same. Below the Girls as example.

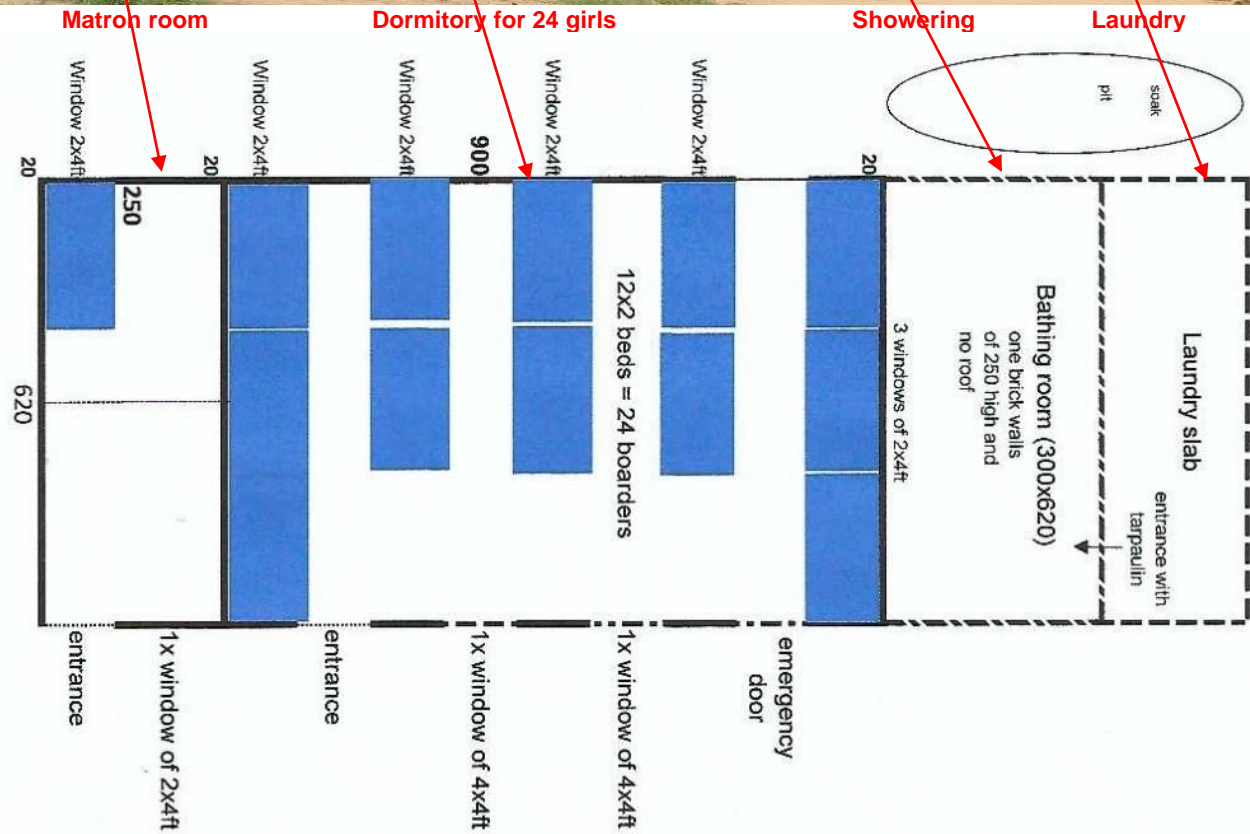

The Toilets for the girls are ca. 5 meters at the right of the laundry slab.

The same holds for the boys, but then at the left of the laundry slab



**Both the Girls and the Boys need water for showering and doing the laundry.**

**There are 4 tanks of 12.000 liters each, which are filled by a pump from a borehole on community land nearby.**

**Those tanks are located left of the Main Hall, substantially higher than the dormitories.**



**Water will flow by gravity from the last tank to a point after the tanks at the Kitchen.**

**From here it will flow by gravity to the showering room and laundry slab of both the girls dormitory and the boys dormitory (see pictures below).**

**Quality of constructions is above par, as experienced during the construction of Kitchen and Main Hall.**



**Forward Planning**

**Rains will soon retreat and will not disturb further progress. We expect to complete the dormitories, including painting by early July. That will be substantially before the new academic year 2021 starts on the 9<sup>th</sup> of August.**

**Inspection Team**

